THE
DIA-LOG
COMPANY
HOUSTON, TEXAS WHITTIER, CALIF.

OIL WELL ELECTRIC LINE SERVICES

CASING PROFILE CALIPER LOG

COMPANY UNION OIL OF CALIFORNIA
WELL COVE FORT - SULPHURDALE UNIT #42-7
FIELD WILDCAT
COUNTY BEAVER STATE UTAH
LOG NO. 40826 DATE FEBRUARY 22, 1978
FOOTAGE LOGGED 1345' VERTICAL SCALE 5" = 100'
ZERO POINT KELLY BUSHING (14' AGL)

CASING RECORD

SIZE	WEIGHT POUNDS PER FOOT	DEPTHS		NOMINAL DIMENSIONS		
		FROM	TO	OUTSIDE DIAMETER	INSIDE DIAMETER	WALL THICKNESS
13-3/8"	54.5	0	1345	13.3750	12.615	.380

REFERENCE DATA

REMAINING WALL THICKNESS INCHES		PERCENTAGE OF NOMINAL WALL THICKNESS REMAINING FOR EACH CASING WEIGHT			REMAINING WALL THICKNESS INCHES		PERCENTAGE OF NOMINAL WALL THICKNESS REMAINING FOR EACH CASING WEIGHT		
		54.5 LBS. PER FT.	LBS. PER FT.	LBS. PER FT.			54.5 LBS. PER FT.	LBS. PER FT.	LBS. PER FT.
9/16	18/32					9/32	74.0		
	17/32				1/4	8/32	65.8		
1/2	16/32					7/32	57.6		
	15/32				3/16	6/32	49.3		
7/16	14/32					5/32	41.1		
	13/32	106.9			1/8	4/32	32.9		
3/8	12/32	98.7				3/32	24.7		
	11/32	90.5			1/16	2/32	16.5		
5/16	10/32	82.2				1/32	8.2		
						0	0		

CONDITION OF CASING BY JOINTS

JOINTS	REMAINING WALL	JOINTS	REMAINING WALL	JOINTS	REMAINING WALL
6	11/32				
11	10/32				
17	9/32				

TOTAL NO. OF JOINTS LOGGED 34

GL04408_3

REMARKS

REMAINING
WALL THICKNESS

NOMINAL O.D.

0 $\frac{1}{8}$ $\frac{1}{4}$ $\frac{3}{8}$ $\frac{1}{2}$

$\frac{2}{32}$ $\frac{6}{32}$ $\frac{10}{32}$ $\frac{14}{32}$ $\frac{18}{32}$

DEPTHS	JOINT NOS.	JOINT CONDITION
	Hanger Joint	11/32
	1	10/32
100'	2	11/32
Tool Hang		
	3	11/32
Tool Hang		
	4	11/32
200'		
	5	11/32



THE DI-LOG CO. CHART NO PC-940

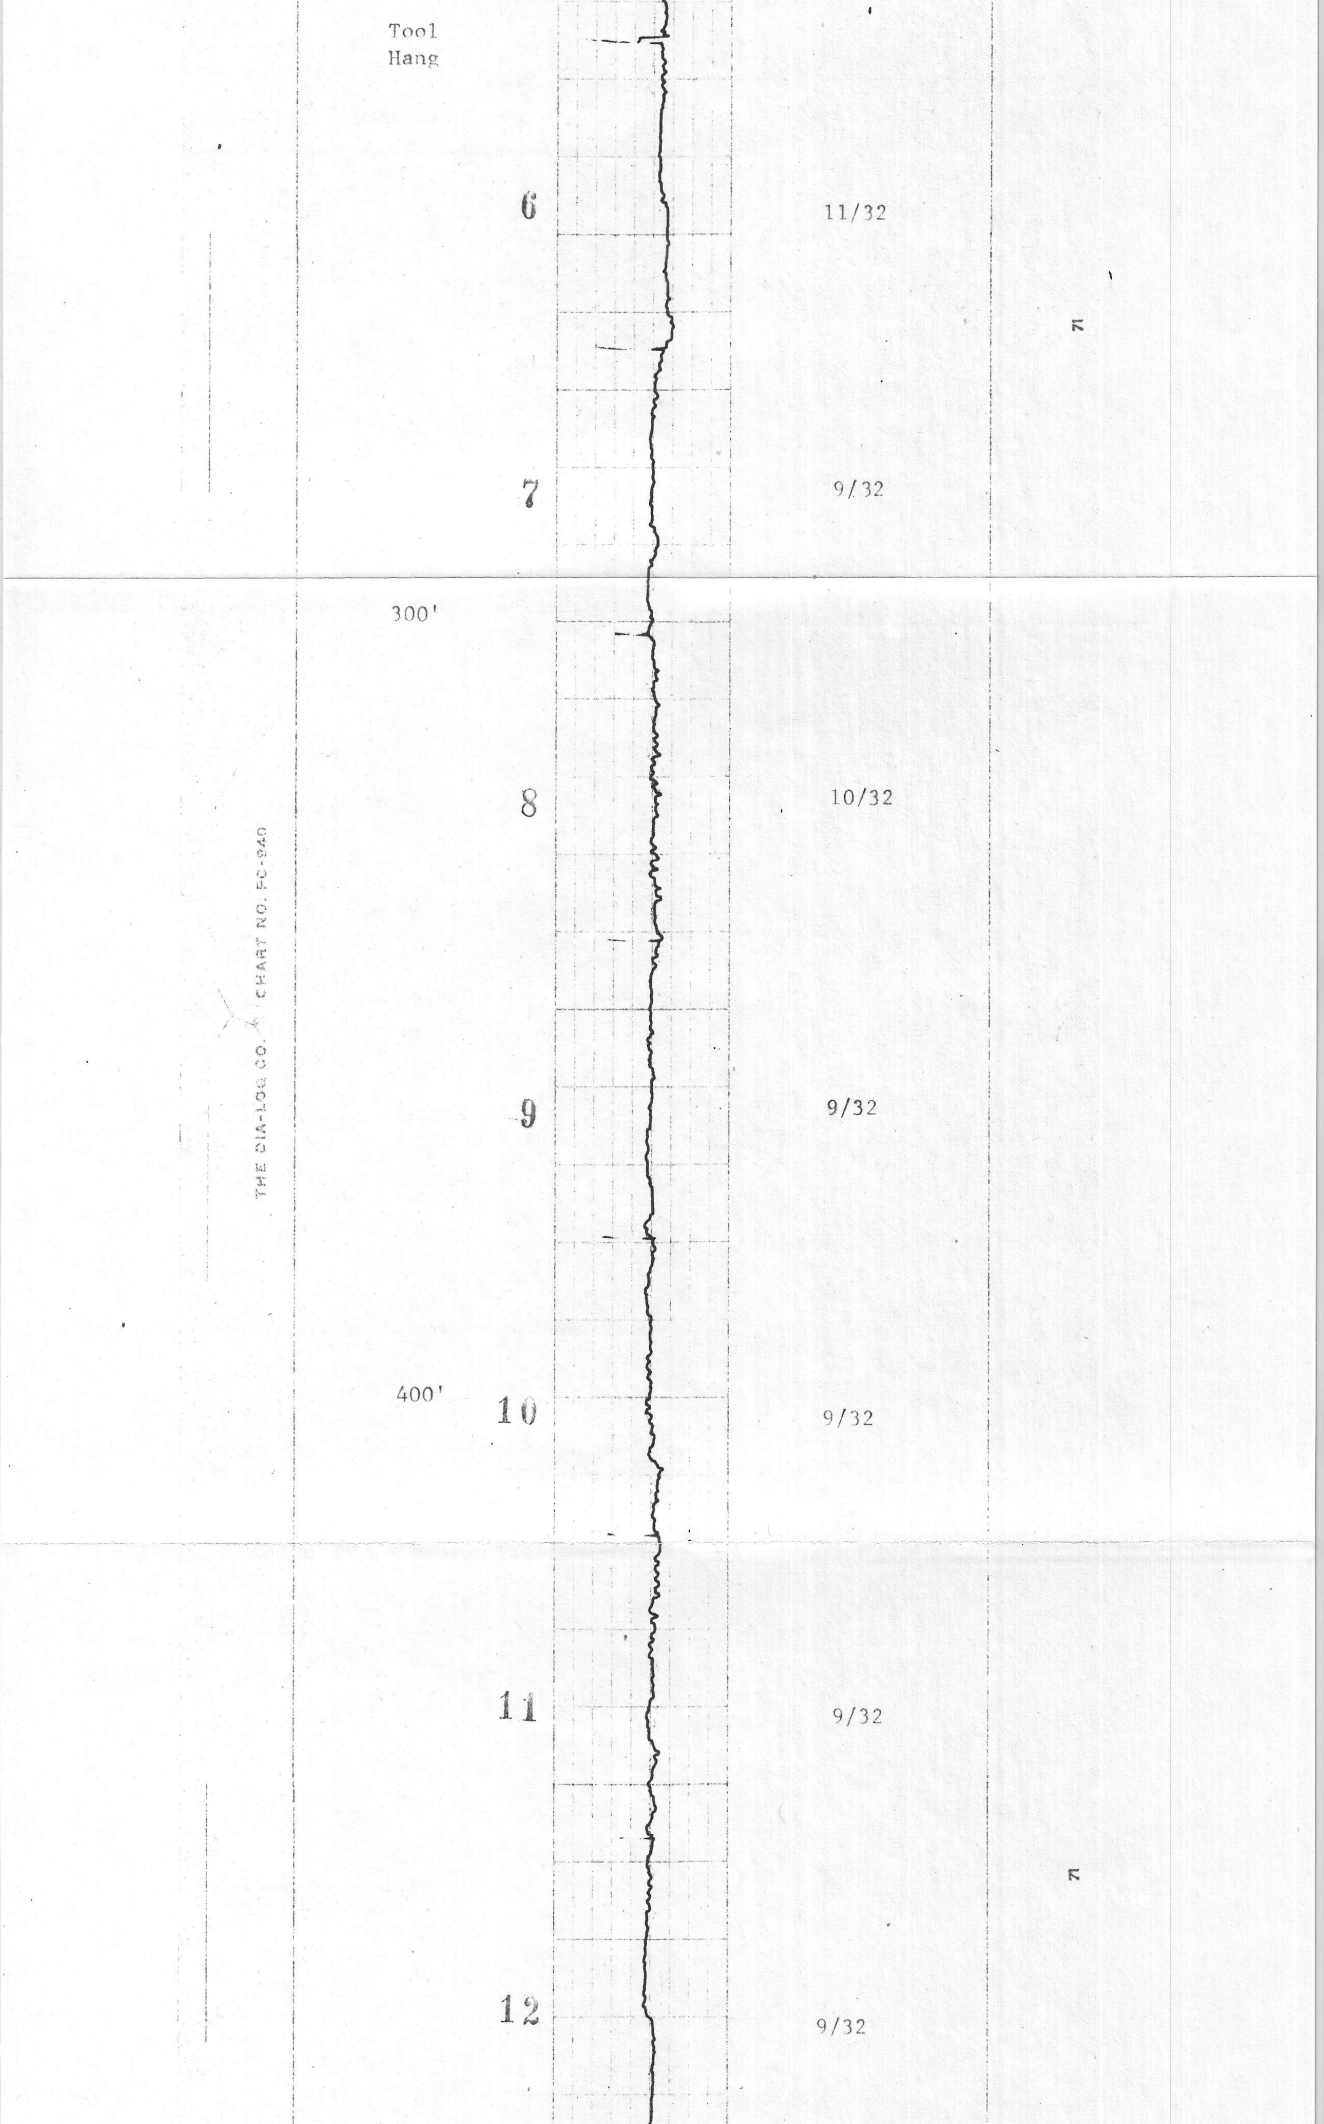

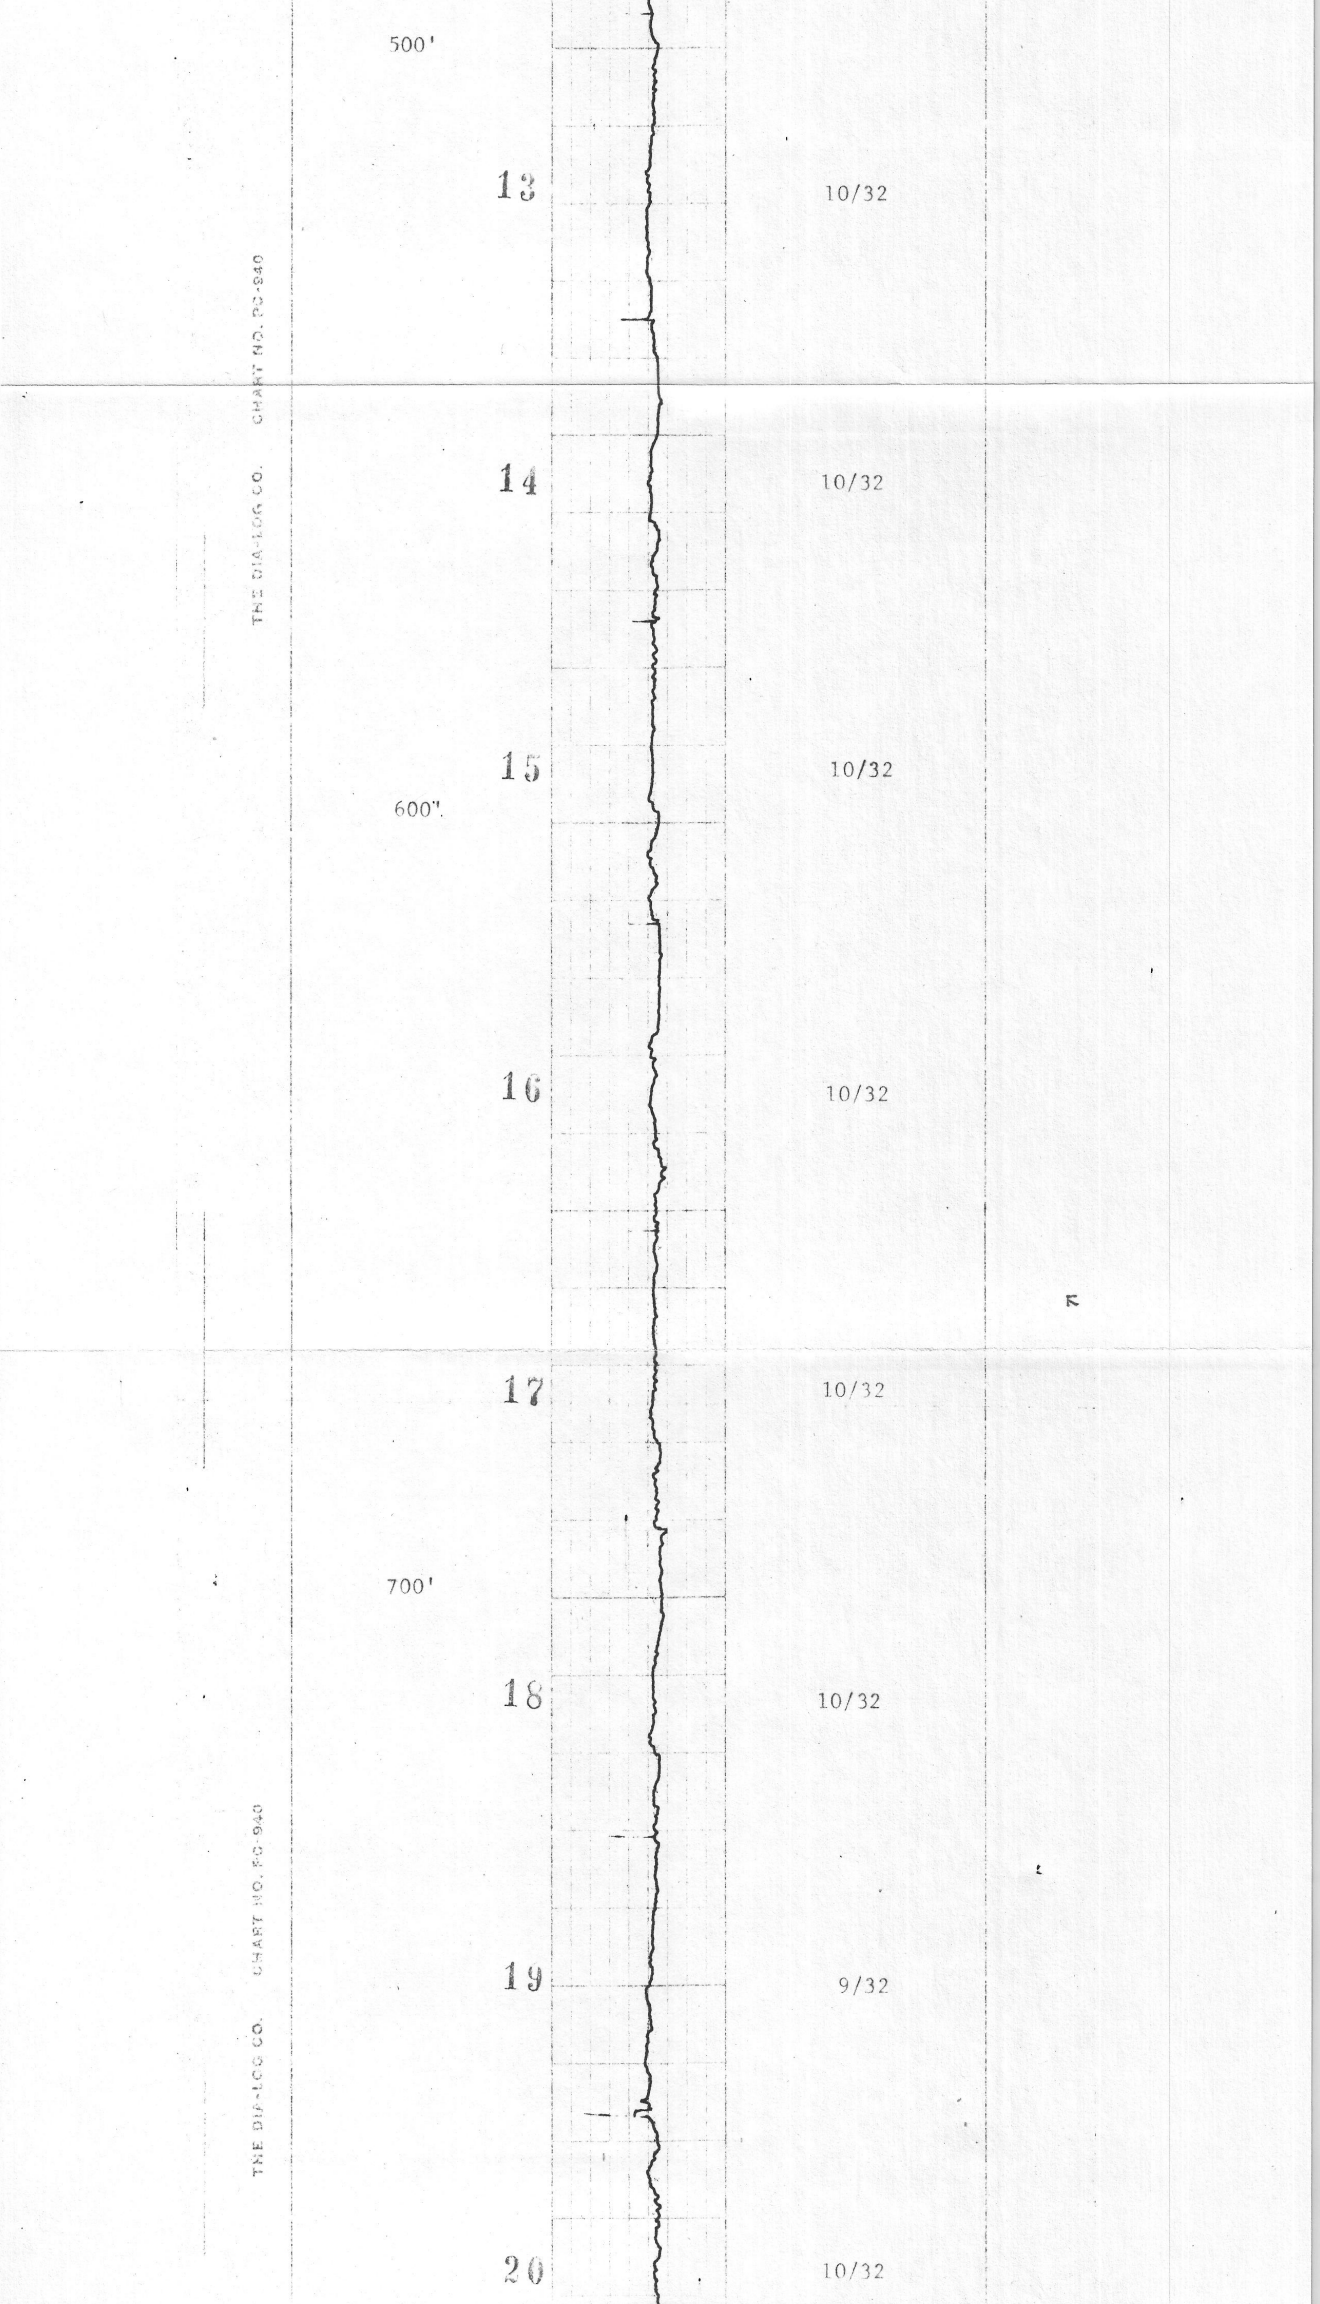

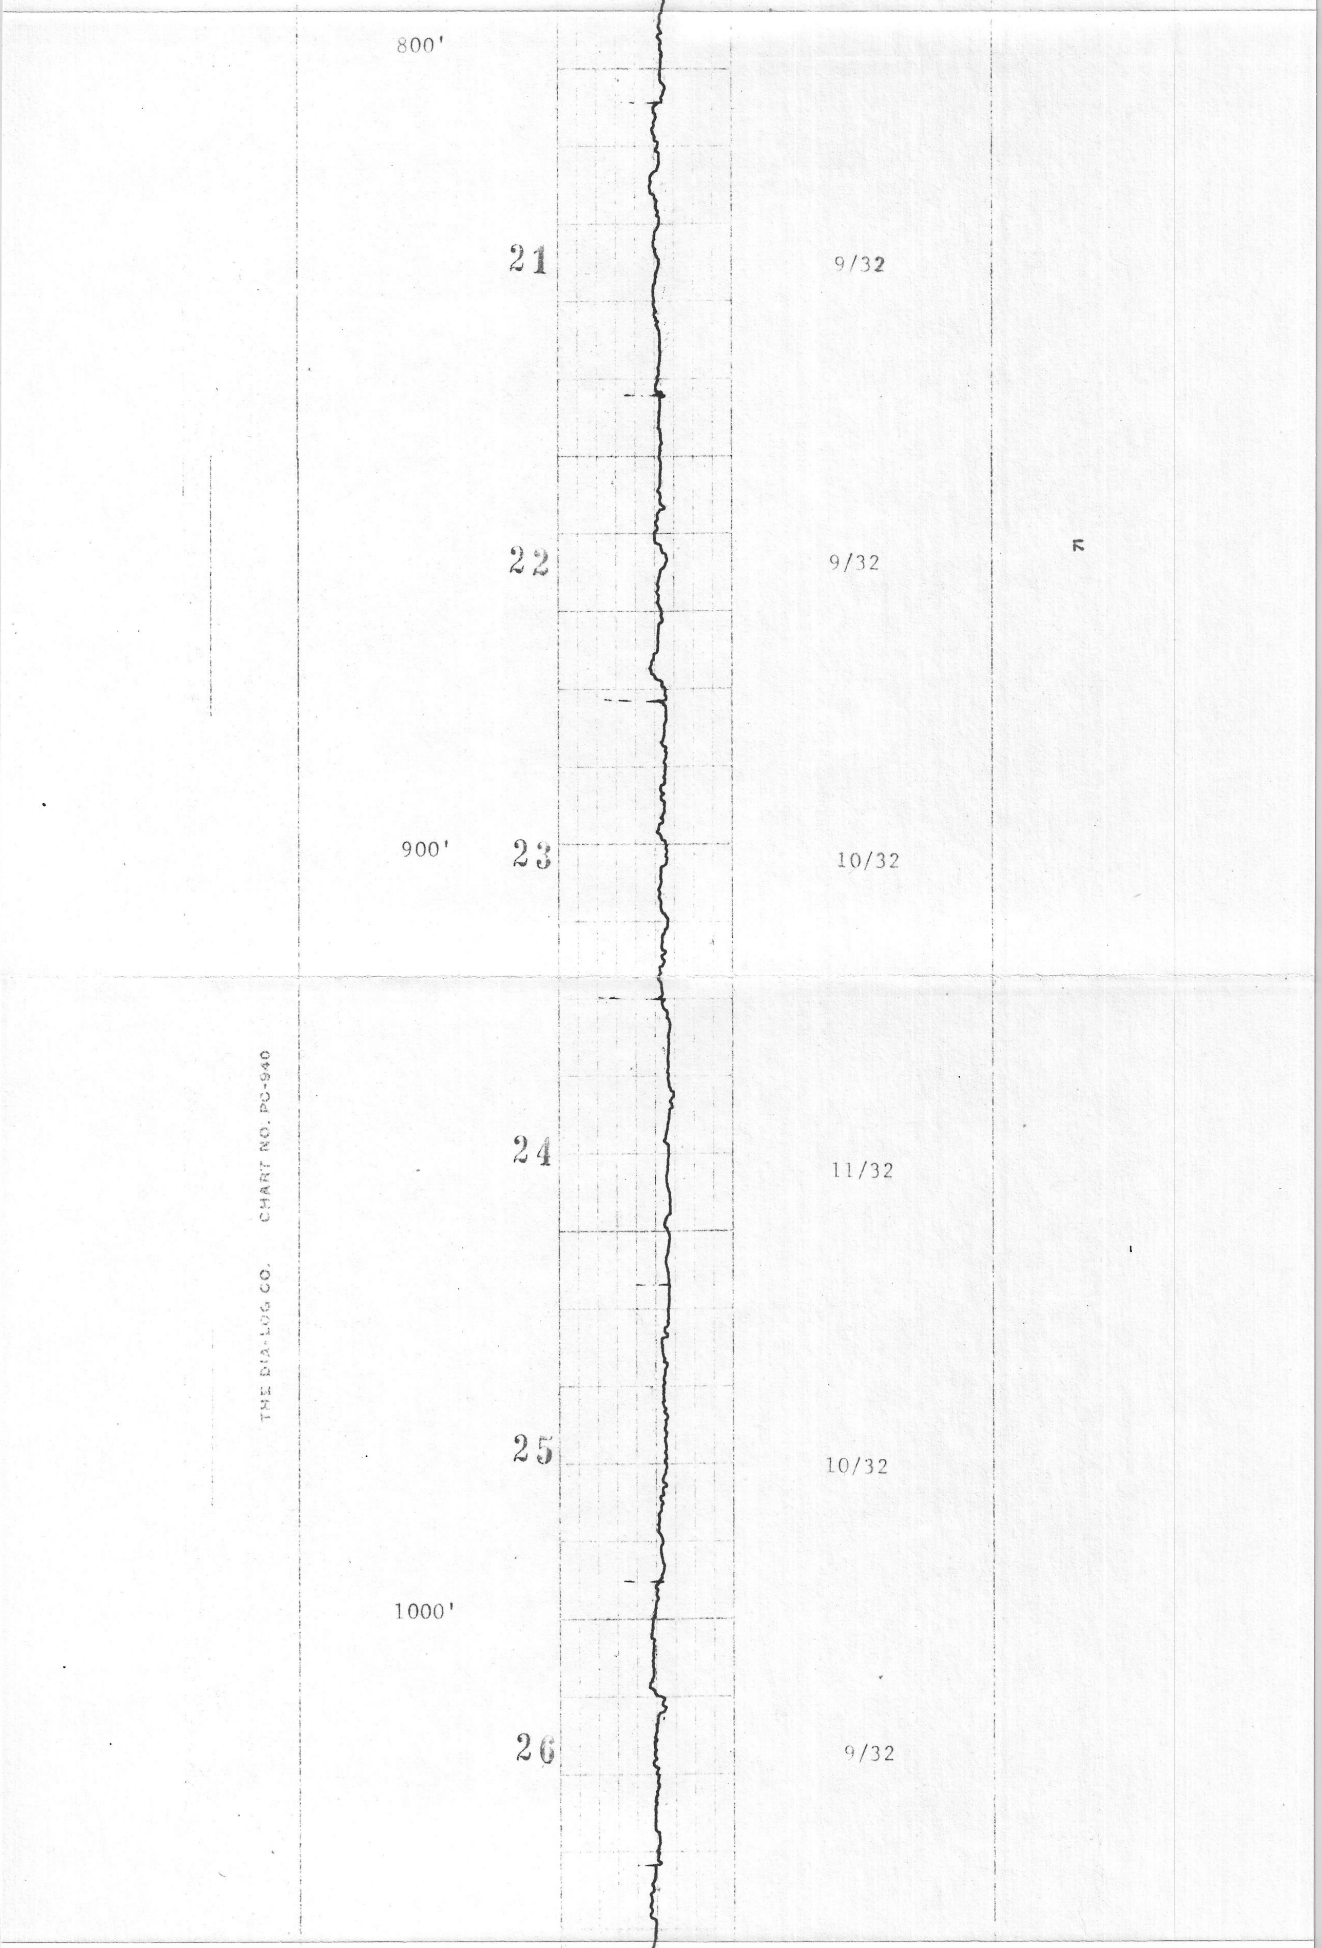

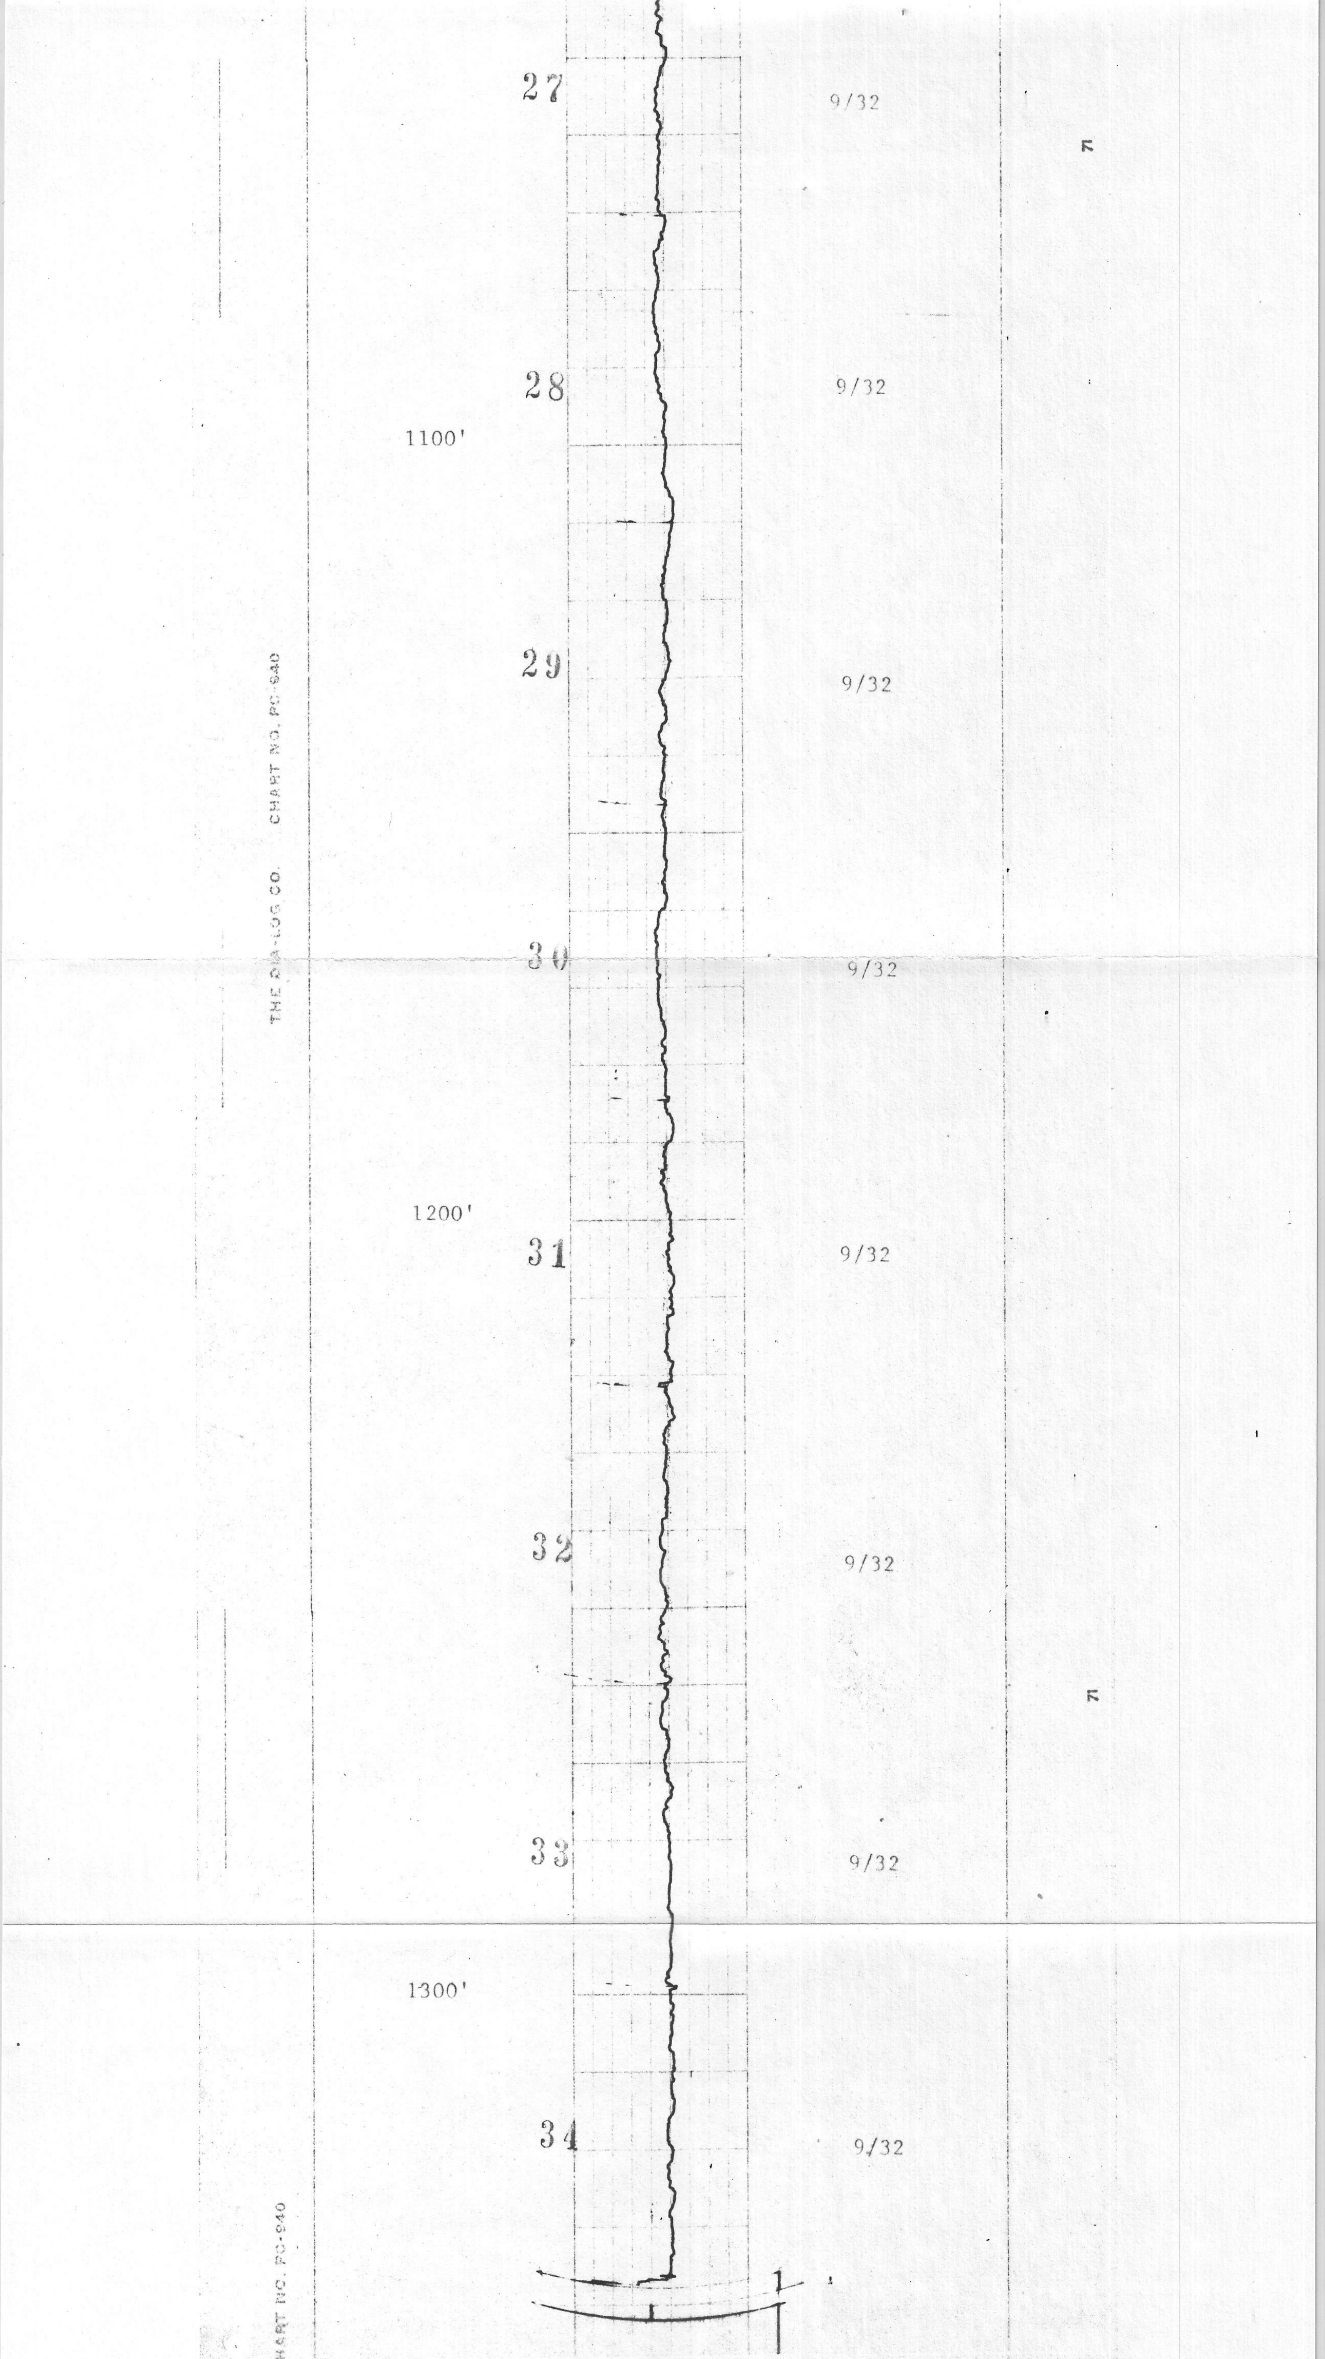

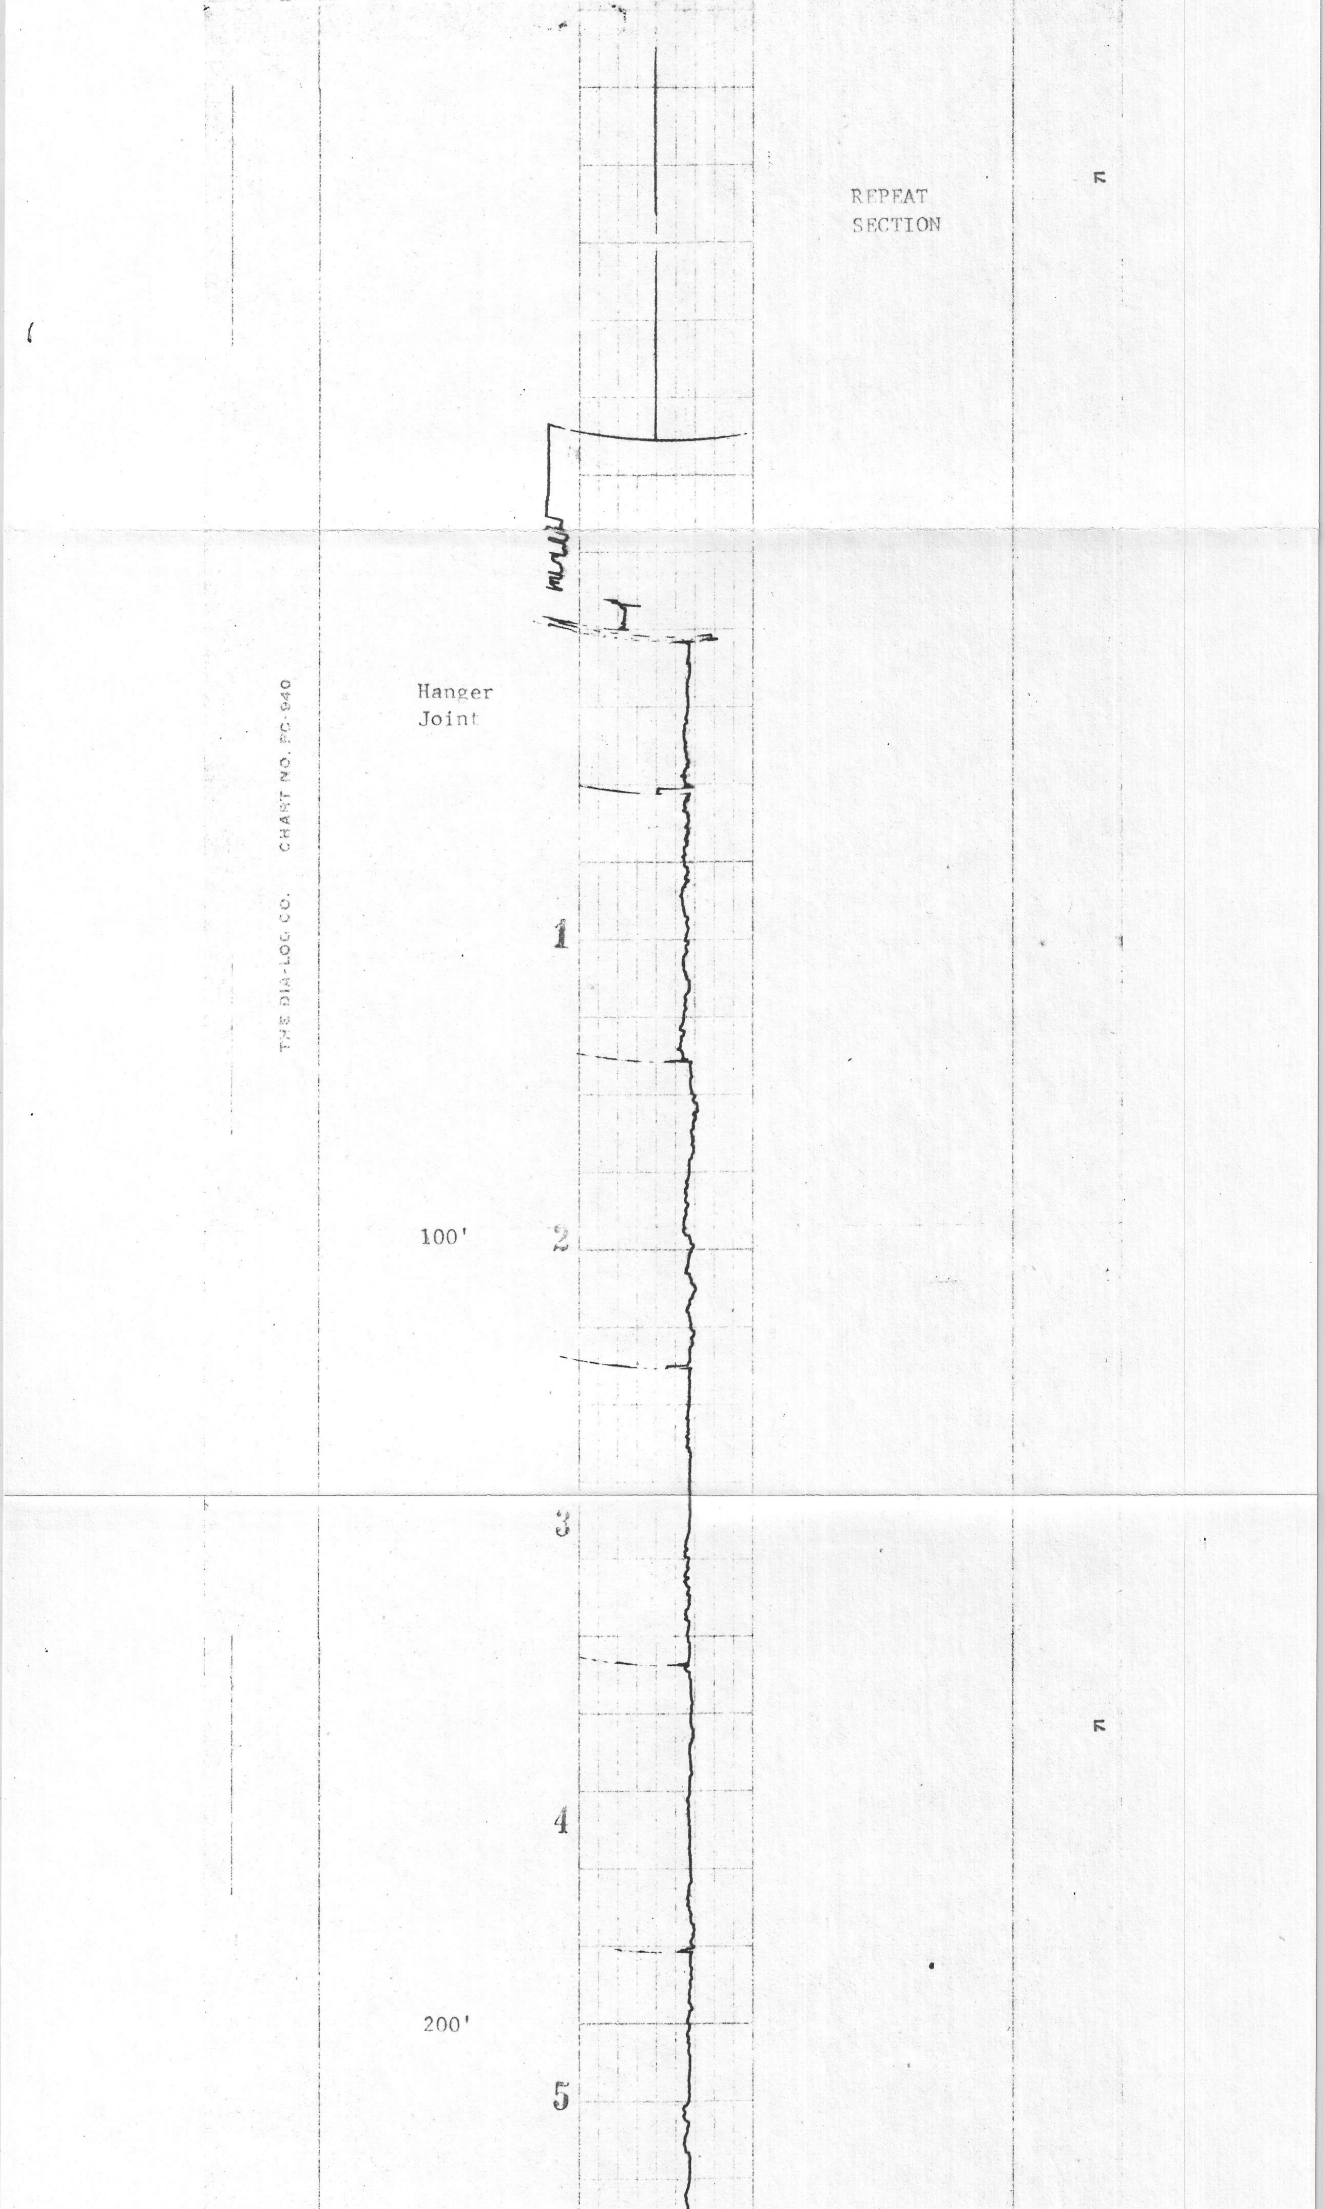

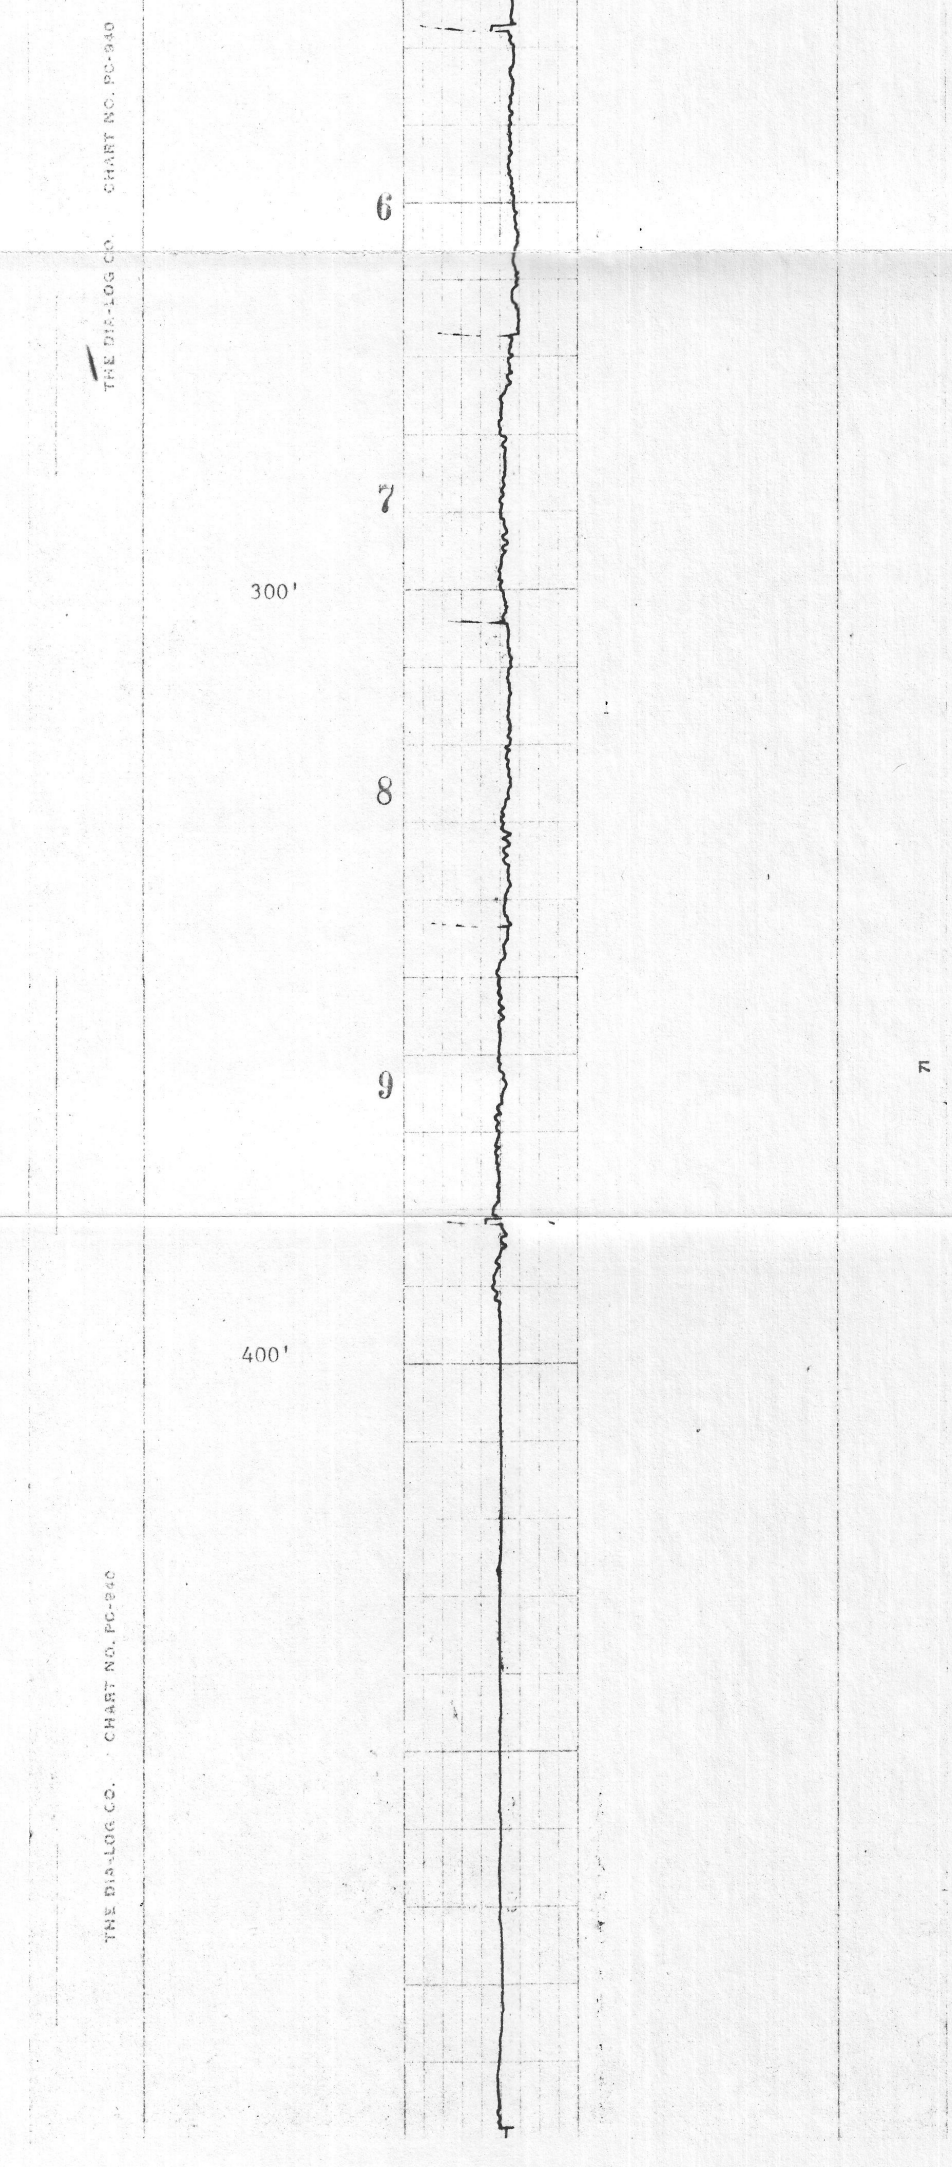
THE DIA-LOG CO. CHART NO. PC-940
6
7
300'
8
9
400'
THE DIA-LOG CO. CHART NO. PC-940
