GL04395

ATLAS WIRELINE SERVICES

TPS PROLOG®

FILE NO. **2979**

API NO.

2" = 100'

COMPANY	MISSION POWER
WELL	AIDLIN NO.8
FIELD	GEYSERS
COUNTY	SONOMA
STATE	CALIF.

LOCATION:
150' NORTH AND 590' WEST
OF SOUTHEAST CORNER SECTION 32

SEC 32 TWP 12N RGE 9W

OTHER SERVICES
CAL/GR
TPS

PERMANENT DATUM G.L. ELEV. 1996
LOGGING MEASURED FROM K.B. 29 FT. ABOVE P.D.
DRILLING MEASURED FROM K.B.

ELEVATIONS
KB 2025
DF NA
GL 1996

DATE	12/23/88	
RUN	1	
SERVICE ORDER	169581	
DEPTH-DRILLER	10818	
DEPTH-LOGGER	10575	
BOTTOM LOGGED INTERVAL	10575	
TOP LOGGED INTERVAL	100	
TYPE FLUID IN HOLE	STEAM	
SALINITY PPM CL.		
DENSITY LB/GAL.		
LEVEL	FLOWING	
MAX. REC. TEMP. DEG. F	553F	
OPR. RIG TIME	7 HRS.	
EQUIP. NO. / LOC.	6352 | BAK.	
RECORDED BY	LENOIR	
WITNESSED BY	MR. JOHNSON	

FINAL PRINT
LAC ANALYSIS

BOREHOLE RECORD

NO.	BIT	FROM	TO
ONE	8 1/2"	8939	10818

FOLD HERE

IN MAKING INTERPRETATIONS OF LOGS OUR EMPLOYEES WILL GIVE CUSTOMER THE BENEFIT OF THEIR BEST JUDGEMENT, BUT SINCE ALL INTERPRETATIONS ARE OPINIONS BASED ON INFERENCES FROM ELECTRICAL OR OTHER MEASURMENTS, WE CANNOT, AND WE DO NOT GUARANTEE THE ACCURACY OR CORRECTNESS OF ANY INTERPRETATION. WE SHALL NOT BE LIABLE OR RESPONSIBLE FOR ANY LOSS, COST, DAMAGES, OR EXPENSES WHATSOEVER INCURRED OR SUSTAINED BY THE CUSTOMER RESULTING FROM ANY INTERPRETATION MADE BY ANY OF OUR EMPLOYEES.

Western Atlas International
A Litton/Dresser Company

ATLAS WIRELINE SERVICES

CASING RECORD

SIZE	WGT	FROM	TO
13 3/8	68	GL	4973
10 3/4	40-45	GL	4650
9 5/8	43	4650	8939

REMARKS RUN (1)

SURFACE DAT TEMP. 403F ,PRESS.139PSIG
FLOW RATE 156,000PPH
FLOWMETER RESTRICTOR SET 1"BOTTOM,TOP 1/2"
SPINNER 1.17"DIA.,3' PITCH ,4 BLADES
STARTED LOG 07;15,REACHED TD AT 08:30
MAX. THERMS: 556°F,554°F.

EQUIPMENT DATA

RUN	TRIP	TOOL	SERIAL NO.	SERIES NO.	POSITION
1	1	TEMP	94149	2173XA	CENT
1	1	PRES	94147	2175XA	CENT

MISSION POWER
AIDLIN NO.8

[illegible]
[illegible]

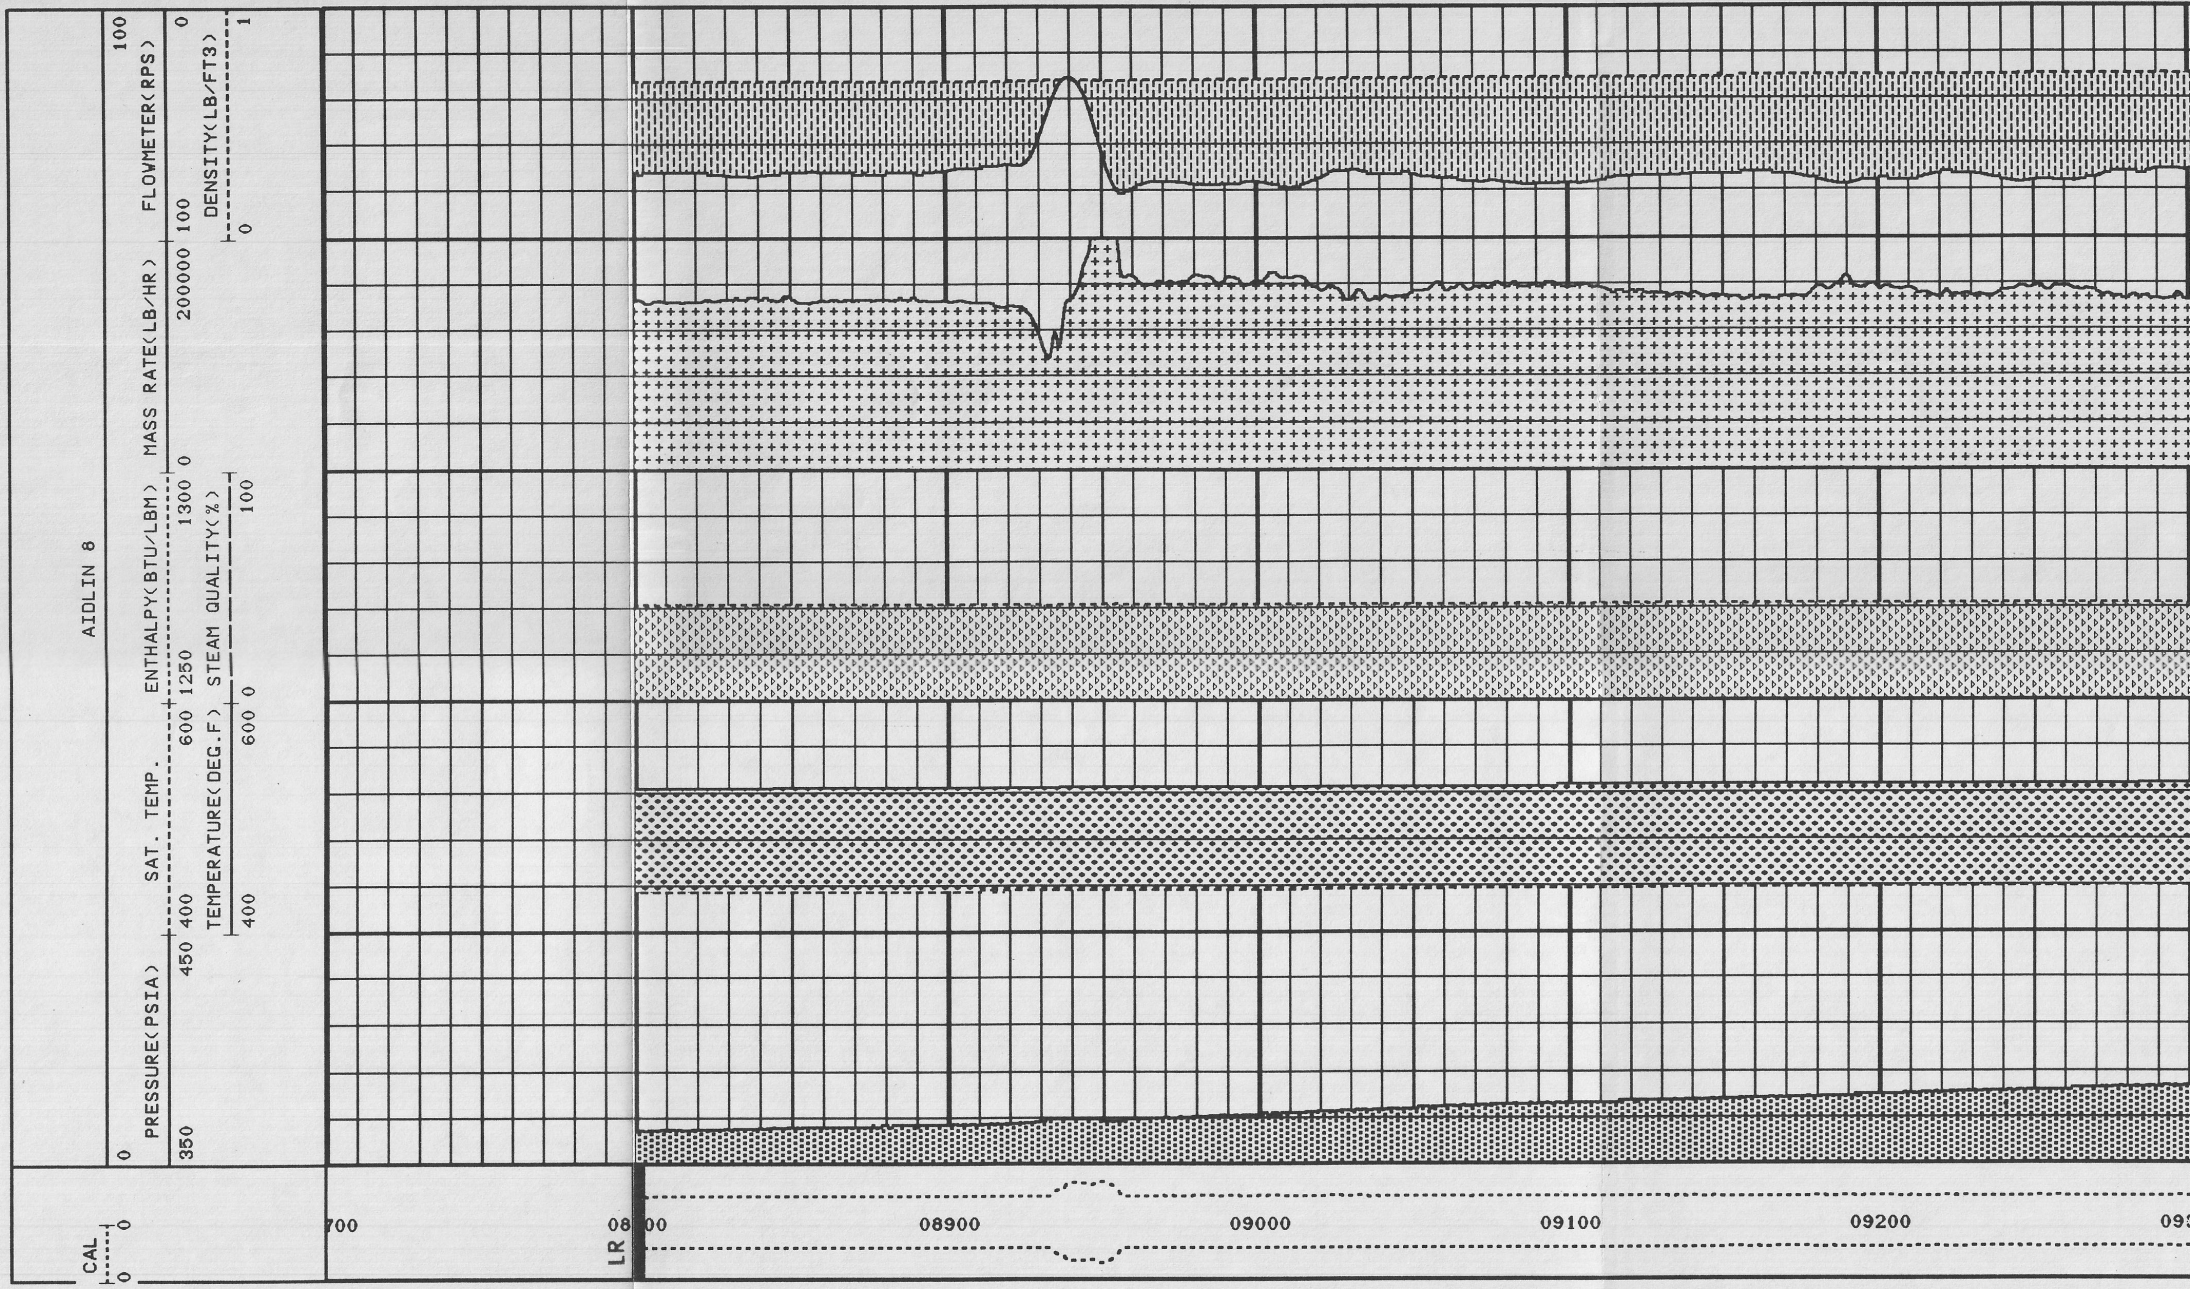

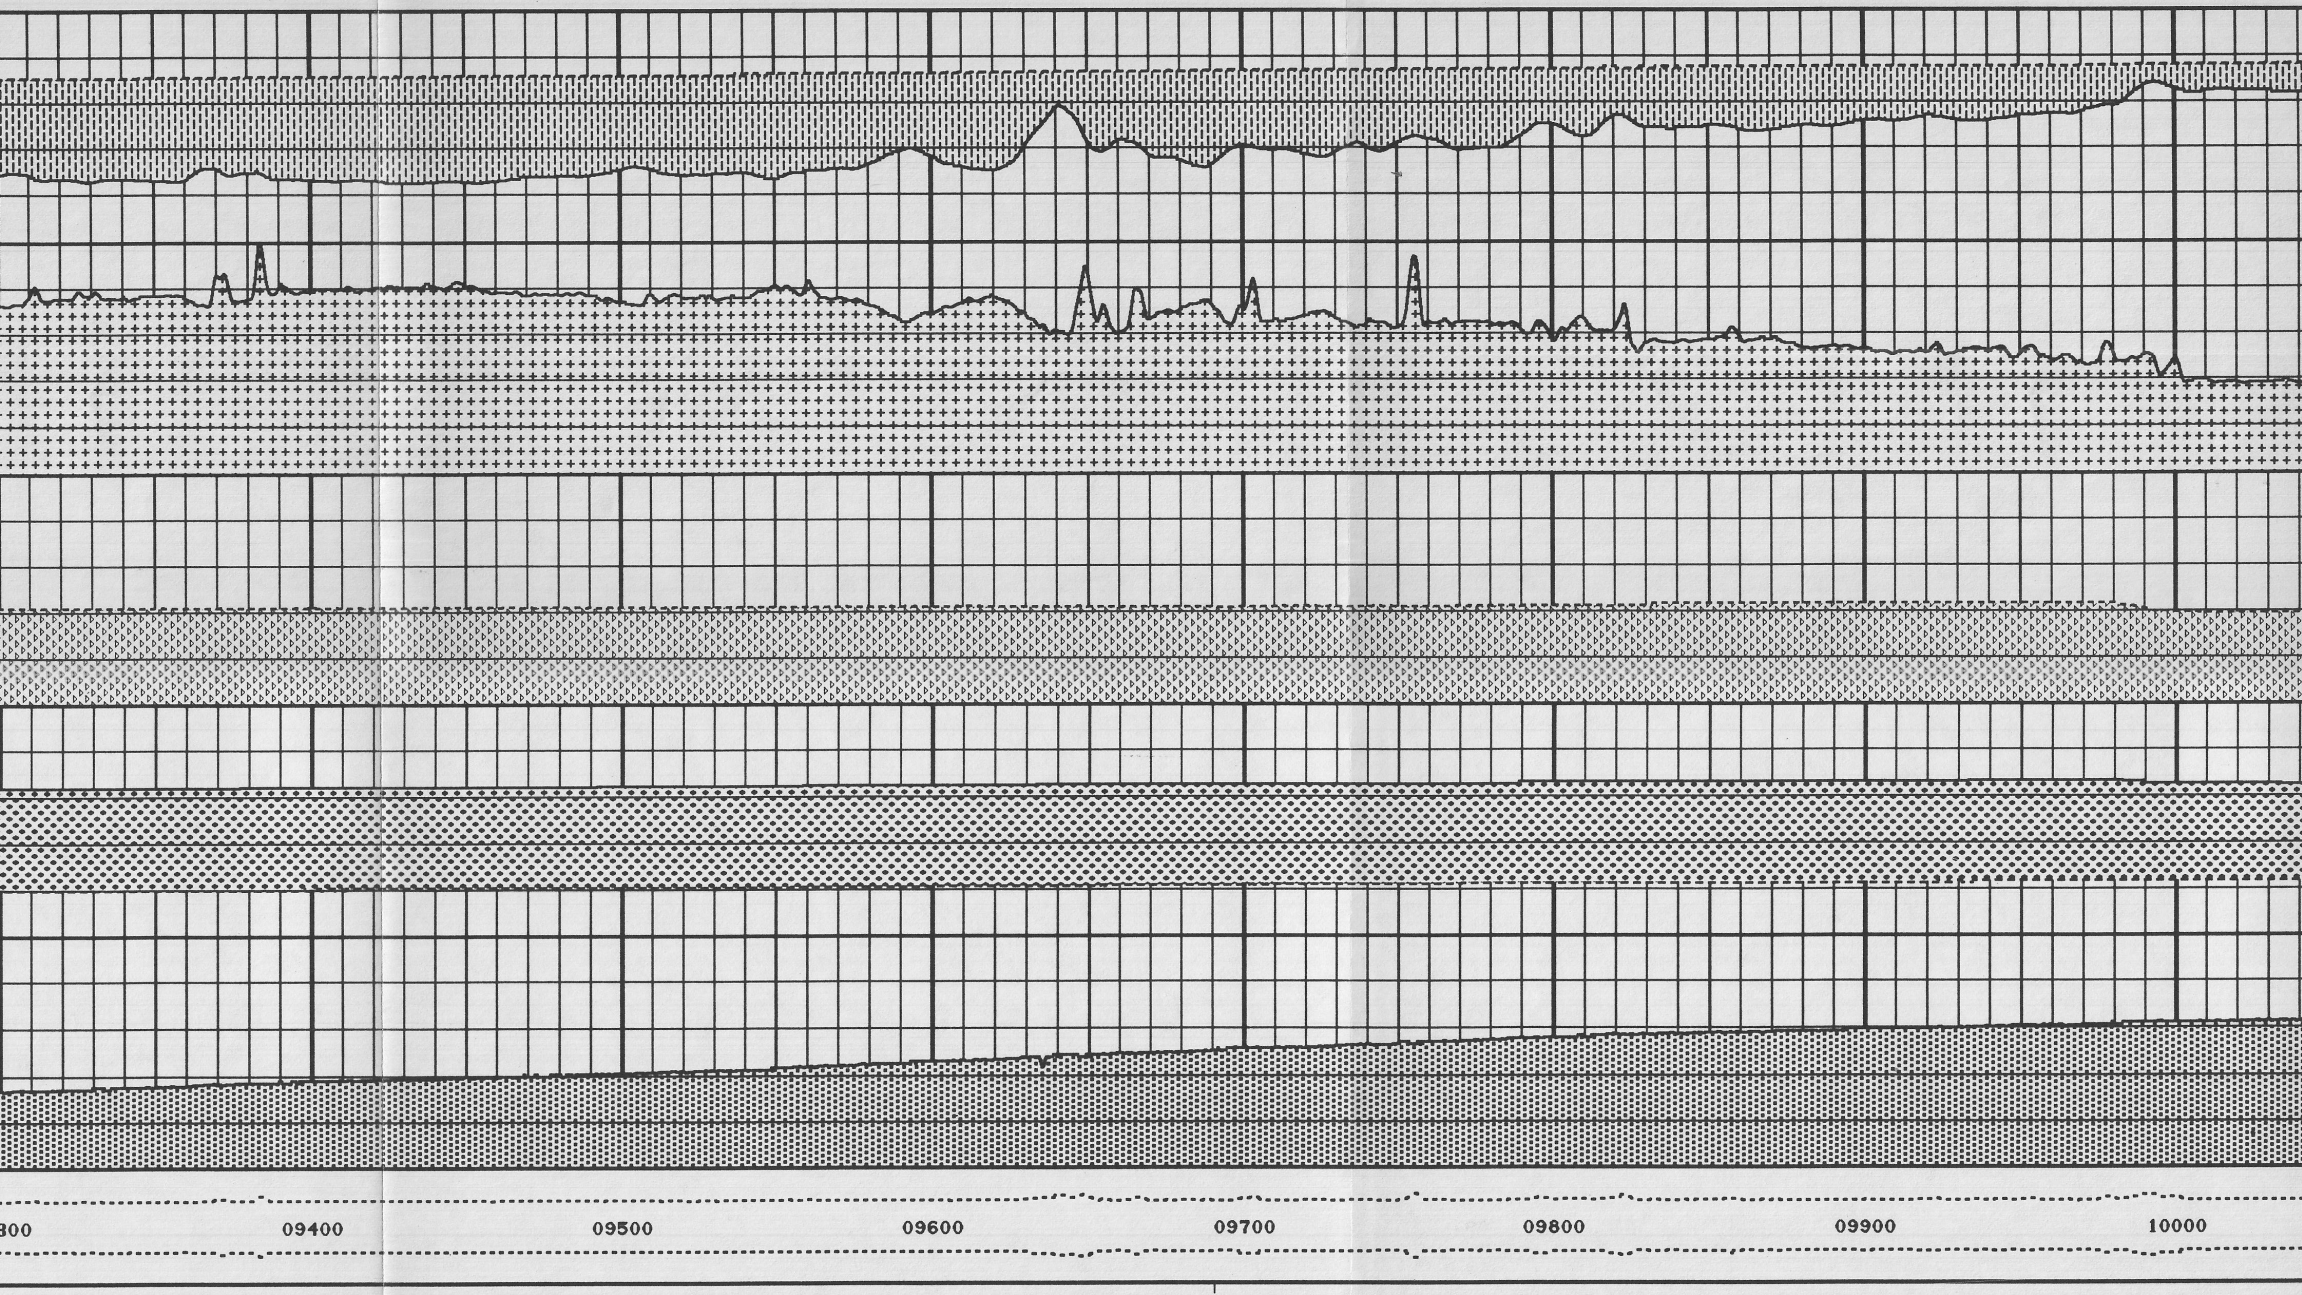

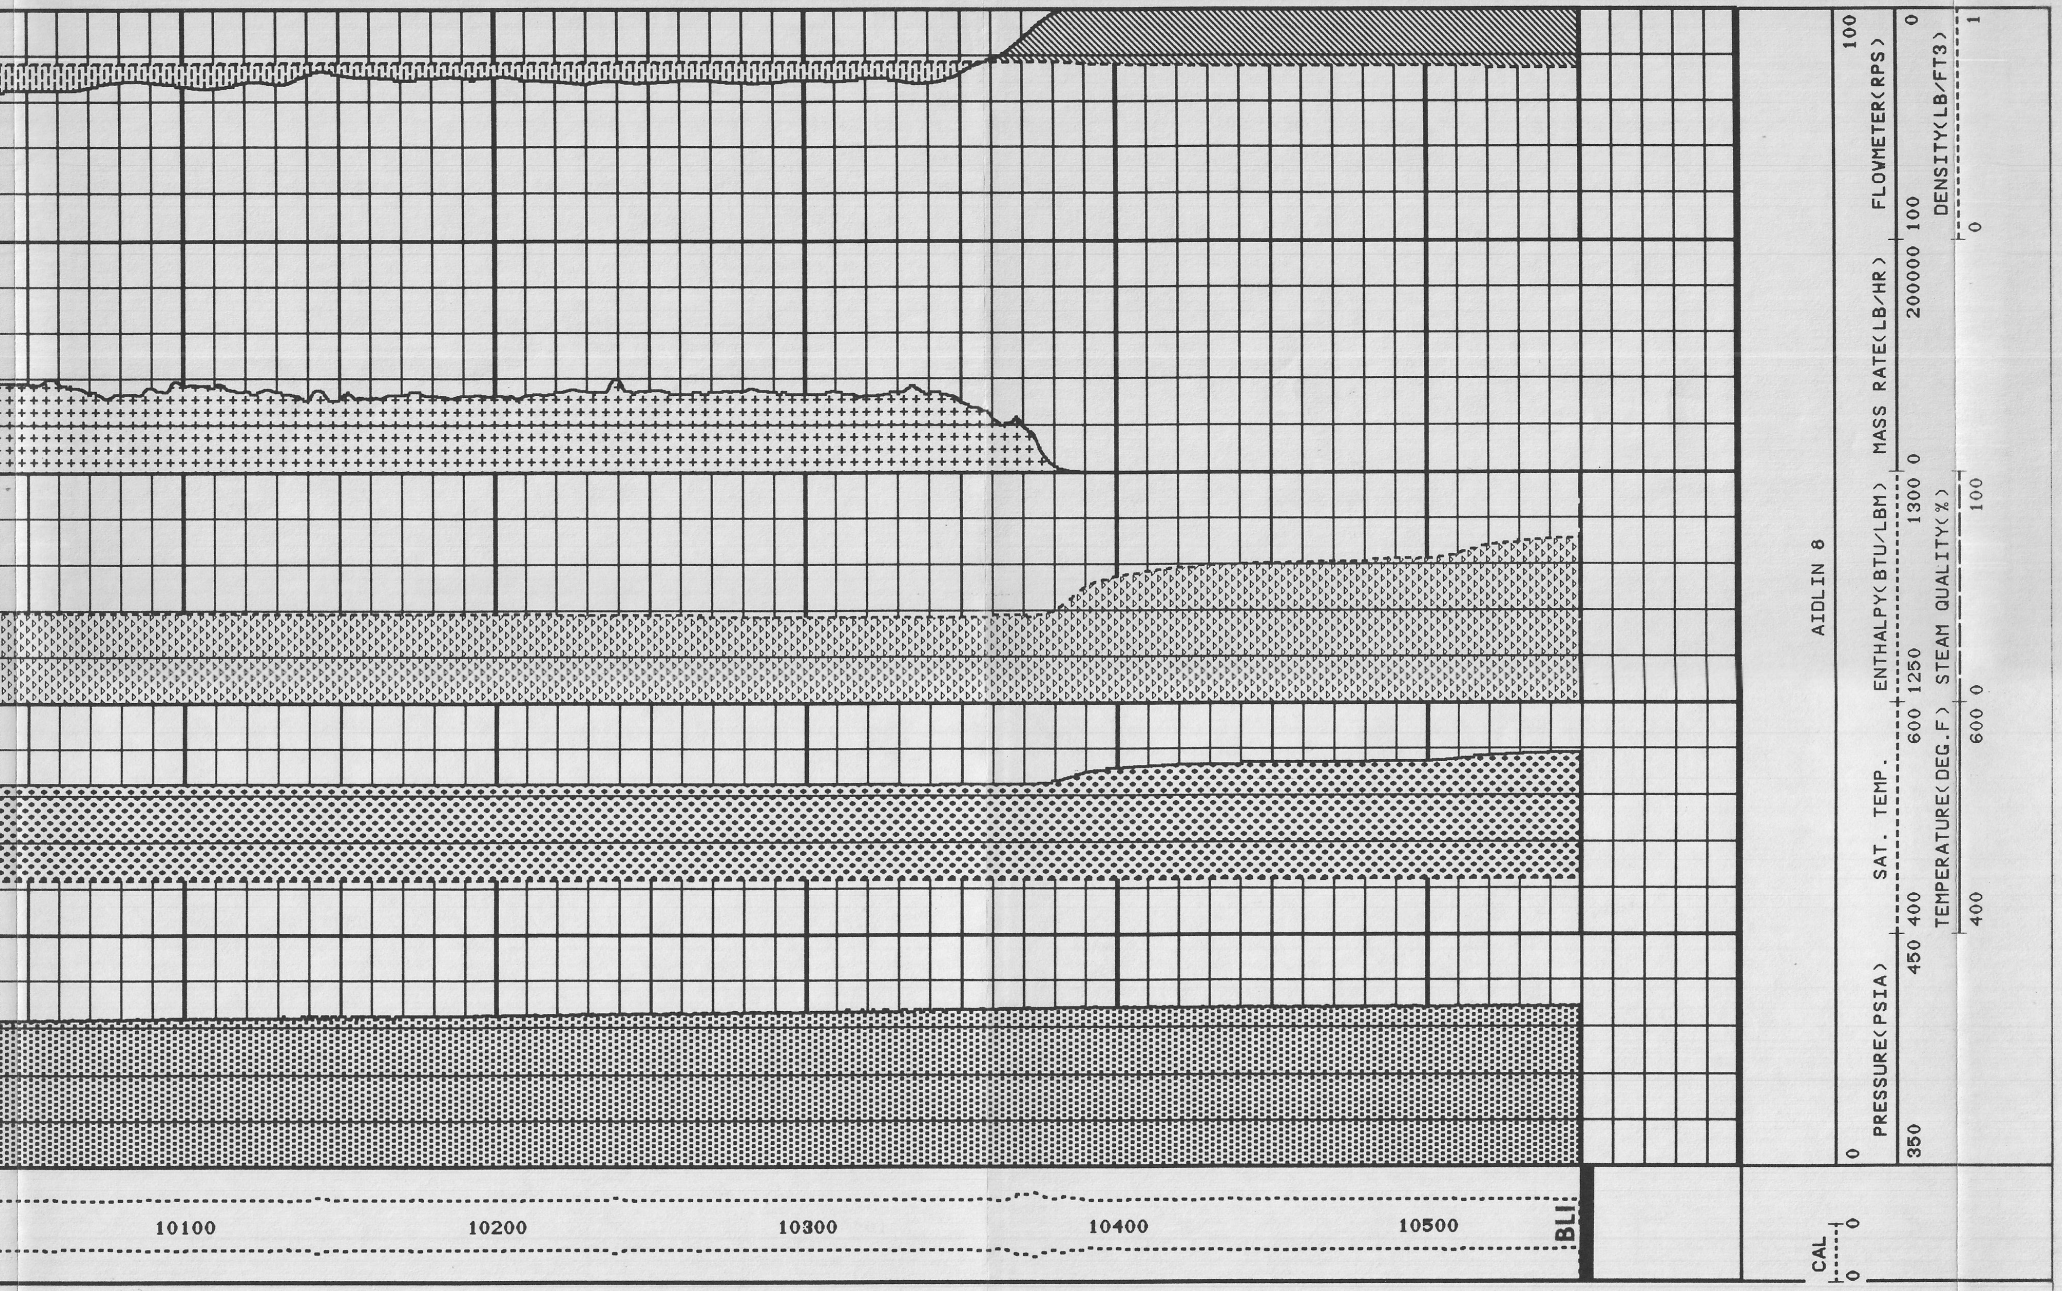

```
      DEP          GRC          TEMP         TSAT         ETD1         DENM         DIAM         FSPN         MFLO

   10550.00       419.00       557.21       448.76      1285.86        0.75         8.40         0.00       540.66
   10500.00       418.45       549.87       448.63      1281.39        0.76         8.54         0.00       531.88
   10450.00       418.72       548.32       448.69      1280.39        0.76         8.65         0.00       526.24
   10400.00       418.46       543.43       448.63      1277.34        0.76         8.21         0.00       525.10
   10350.00       417.53       530.08       448.41      1268.86        0.78         8.50        28.04     61660.18
   10300.00       417.07       530.04       448.30      1268.88        0.78         8.60        30.20     67828.06
   10250.00       416.14       530.18       448.08      1269.07        0.77         8.53        31.54     69375.06
   10200.00       415.12       530.54       447.84      1269.41        0.77         8.60        29.20     65207.42
   10150.00       414.49       530.53       447.69      1269.48        0.77         8.58        27.76     61667.04
   10100.00       413.92       530.54       447.56      1269.55        0.77         8.78        32.80     76062.94
   10050.00 .     413.19       530.63       447.38      1269.68        0.77         8.54        34.90     76249.44
   10000.00       412.45       530.96       447.21      1269.97        0.77         9.80        33.49     96111.44
    9950.00       411.05       533.54       446.87      1271.79        0.76         8.57        45.91     99937.12
    9900.00       409.56       533.17       446.52      1271.71        0.76         8.66        48.23    106739.63
    9850.00       408.20       532.97       446.19      1271.72        0.75         8.83        50.32    115254.00
    9800.00       406.20       532.18       445.71      1271.42        0.75         9.11        49.12    119186.69
    9750.00       403.84       531.60       445.14      1271.30        0.75         8.60        58.14    125178.75
    9700.00       401.76       531.11       444.63      1271.20        0.74         9.22        58.63    144360.69
    9650.00       398.69       530.77       443.88      1271.30        0.74        10.63        55.47    179880.00
    9600.00       396.21       530.41       443.27      1271.33        0.73         8.80        62.90    138826.69
    9550.00       393.39       529.79       442.58      1271.23        0.73         8.83        73.30    161773.69
    9500.00       391.66       529.38       442.15      1271.14        0.72         8.71        69.54    148800.31
    9450.00       389.80       529.11       441.69      1271.17        0.72         8.87        74.38    164047.25
    9400.00       388.09       528.83       441.26      1271.17        0.72         8.77        73.51    157902.63
    9350.00       385.91       528.45       440.72      1271.15        0.71         8.67        73.69    153848.19
    9300.00       384.26       528.07       440.30      1271.09        0.71         8.58        71.68    146031.62
    9250.00       382.26       527.74       439.80      1271.08        0.71         8.64        76.23    156484.44
    9200.00       380.37       527.40       439.32      1271.06        0.70         8.78        75.56    159282.50
    9150.00       378.52       527.00       438.85      1271.00        0.70         8.67        73.10    149602.75
    9100.00       376.82       526.69       438.42      1270.99        0.70         8.69        76.88    157476.81
    9050.00       374.44       526.25       437.81      1270.95        0.69         8.79        72.60    151338.94
    9000.00       371.93       525.80       437.16      1270.93        0.69         8.94        76.09    162671.19
    8950.00       369.23       525.46       436.46      1271.00        0.68        13.94        60.42    312276.88
    8900.00       367.16       525.00       435.92      1270.92        0.68         8.78        71.70    146028.69
    8850.00       366.22       524.70       435.68      1270.83        0.68         8.89        72.10    150160.69
    8800.00       364.52       524.42       435.23      1270.84        0.67         8.72        72.64    145679.75

** INTERVAL AVERAGES -----------------------------------------------------------------------------
       0.00       397.20       531.17       443.45      1271.68        0.73         8.78        51.89    113535.00


   MISSION POWER                                                                             □Γ□/□Y□□
   AIDLIN NO.8                                                                               □∋□4□

        SERVICE TABLE ***GTHML ***        FILE LABEL # 1

   TAPE  LEVEL SPACING : 0.50    TAPE STARTING DEPTH :   10550.00
   PRINT LEVEL SPACING : 0.00    TAPE ENDING   DEPTH :    8800.00


                    ** UNITS OF MEASURE **

                     DEPTH            FT
                     ACOUSTIC         US/FT
                     CALIPER          IN
                     TENSION          LBS
                     TEMPERATURE      F
                     PRESSURE         PSI
                     VOLUME           FT3


                     *** END OF LIST ***
```
